

Project Plan

ABC Restaurant HCM

Primary Instructor	Anjana Shah
Team Member	Charles Langmuir
Team Member	Joel Chandra Paul
Team Member	Yueyang Peng
Team Member	Jingyu He

Document Revision History

Revision #	Date
1.01	2025-10-01
1.02	2026-01-28

Table of Contents

1. Executive Summary

The following describes the project to be executed.

Objective	To create an HCM application with a functional and secure backend that will be tailored to small to medium sized restaurants in Toronto.
Corporate Goals Addressed	-Reduce managerial workload by automating scheduling and payroll tasks. -Provide employees with self-service tools for availability, time-off, and reimbursement requests. -Improve operational efficiency for SMEs that cannot afford enterprise-level HCM systems.
Planned Start Date	2025-10-06
Planned End Date	2026-03-26

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Project Manager / Technical Lead	Charlie Langmuir	charles.langmuir@georgebrown.ca	2025-10-01
Software Developer	Joel Chandra Paul	Joel.ChandraPaul@georgebrown.ca	2025-10-01
Business Analyst	Yueyang Peng	yueyang.peng@georgebrown.ca	2025-10-01
Quality Assurance / Testing Lead	Jingyu He	jingyu.he@georgebrown.ca	2025-10-01

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
Web application for the software	On-site backup servers
Integrated scheduling and payroll services	Corporate level tax filing software
Employee requests: time-off, shift changes, reimbursements.	Integration to pre-existing payroll services
Notifications (shift reminders, approvals).	AI integration
A support ticket service that allows end user to request assistance from the project team	

4. Deliverables

This project will deliver the following.

Deliverable	Description
Functional Web Application	A working browser-based HCM system for small to medium restaurants. Core features: scheduling, payroll, expense reimbursement, and notifications.
Backend System & Database	Secure backend to handle data storage, scheduling logic, payroll processing, and employee/manager requests.
Role-Based User Management	Implementation of access control for different roles (Manager, Employee, Finance Staff, System Admin) with tailored features.
Documentation	User guide (for managers, employees, finance staff) and technical documentation (system design, database schema, APIs, and deployment).
Final Project Report	A comprehensive report covering problem analysis, requirements, system design, implementation details, testing results, and outcomes.

5. Assumptions

This project makes the following assumptions;

- Restaurant managers will read the documentation and explain to their employees how they will use the application
- Project team members will make themselves available to ensure key deliverables are completed in collaboration
- The project plan is subject to change as new information appears
- The project team will make every effort to ensure all deliverables and documents are completed punctually and properly
- Project team members will conduct the necessary research to ensure the applications functionality and UI appearance are user friendly to meet the needs of the target end users

6. Dependencies

Internal:

- Coordination between team members for punctual work on tasks.
- Availability of completed requirements prior to the development phase.
- Completion of Wireframes and the UI Prototype prior to coding.
- A maintained line of communication between the QA/Testing and Software Development members.

External:

- Access to required development tools.
- Feedback and approvals from Anjana Shah surrounding key milestones.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Technical Complexity	H	M	Implement a simplified version first(manual scheduling + partial automation), expand later if time permits.
Testing Delays(bugs found late in the project)	H	L	Start testing early in development, adopt iterative testing

			approach, and assign a QA lead
Team Availability(conflicts with courses or assignments)	H	H	Define clear roles, create a realistic schedule, and allow flexible task reassignments.
Scope Creep(adding extra features beyond the agreed scope)	M	M	Review scope regularly, focus on core features, record change requests.
Lack of Communication among team members	M	M	Weekly meetings, daily updates on teams, and task tracking via GitHub

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Weekly status/progress report	Project Team	Every Wednesday
Minutes of meeting	Project Team, Instructor	Weekly
Final Project Report	Project Team, Instructor, Stakeholders	Once at project end

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Weekly Team Meeting	Track project progress, and work collaboratively on deliverables and documents	All Team Members	Every Wednesday
Development Start Meeting	Review task distribution and begin development of the application	All Team Members	Once at start of software development


Testing/QA Review	Monitor progress on testing	Testing Team	Monthly once development has begun
Instructor Review	Request feedback from the Instructor(Anjana) on project progress	All Team Members, Anjana Shah	Every Wednesday

9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.

Reference	Tasks	Duration	Dependency
A	Project Vision	2 weeks	N/A
B	Business Requirements	1 week	N/A
C	Personas and User Stories	2 weeks	N/A
D	Project Plan	2 weeks	A,B,C
E	Team Charter	1 week	A,B,C
F	Product backlog	1 week	A,B,C
G	Sprint backlog	1 week	A,B,C
H	Requirement gathering & sign-off	2 weeks	D,E,F,G
I	System Analysis & Design	1 week	D,E,F,G
J	Wireframes & UI Prototype	2 weeks	H,I
K	Technical Requirements	1 week	H,I
L	Backend design & database setup	1 week	J,K
M	Web frontend design (UI/UX)	2 weeks	L
N	Core features: scheduling + payroll	2 weeks	M
O	Employee workflows (time-off, shift swaps, reimbursements)	2 weeks	N
P	Notifications (shift reminders, approvals)	1 weeks	O
Q	Testing & bug fixing	2 weeks	P
R	Documentation	2 weeks	Q
S	Final demo & submission	2 weeks	R

10. Gantt Chart (Revised)

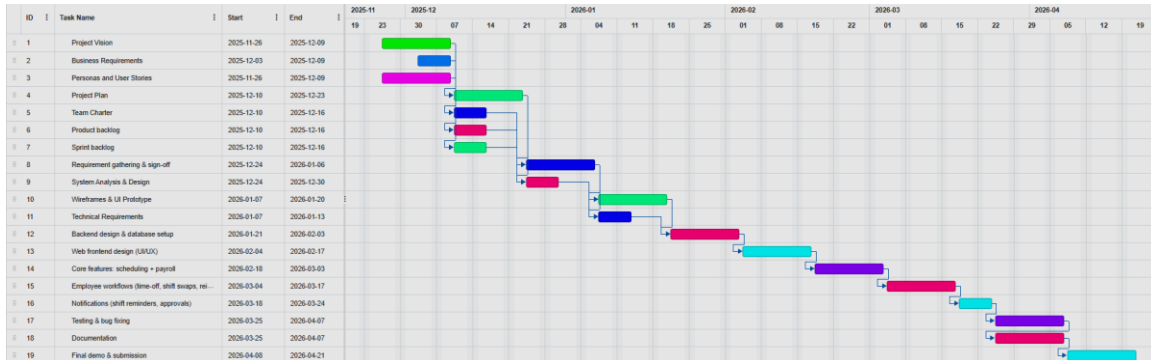

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Project Plan Approved	2025-10-20	Charlie Langmuir / All Team Members
Requirements Gathering & Sign-Off Completed	2025-11-10	Yueyang Peng / Charlie Langmuir
System Design & Technical Requirements Finalized	2025-11-24	Joel Chandra Paul / Yueyang Peng
UI Wireframes & Prototype Completed	2025-12-08	Joel Chandra Paul / Jingyu He
Backend & Database Setup Complete	2026-02-03	Joel Chandra Paul / Charlie Langmuir
Core Features (Scheduling + Payroll) Functional	2026-03-03	Joel Chandra Paul / Charlie Langmuir
Employee Workflows Implemented (Time-off, Reimbursements, Shift Swaps)	2026-03-17	Joel Chandra Paul / Yueyang Peng
Notifications System Functional	2026-03-24	Joel Chandra Paul / Jingyu He
Testing & Bug Fixing Completed	2026-04-07	Jingyu He / All Team Members
Final Demo & Project Submission	2026-04-21	All Team Members / Anjana Shah

12. RAM – Responsibility Assignment Matrix

Project Team Responsibilities

Project Name: ABC Restaurant HCM

Project Manager: Charles Langmuir

Tasks	Charles	Joel	Yueyang	Jingyu
Project Vision	P	S	S	S
Business Requirements	S	-	P	-
Personas & User Stories	P	S	S	S
Project Plan	P	S	S	S
Team Charter	P	P	S	S
Product backlog	S	S	S	P
Sprint backlog	S	S	P	-
Requirement gathering & sign-off	S	S	P	P
System Analysis & Design	S	S	P	S
Wireframes & UI Prototype	S	P	P	-
Technical Requirements	S	P	P	-
Backend design & database setup	-	P	S	-
Web frontend design (UI/UX)	-	P	S	-

Core features: scheduling + payroll	S	P	S	S
Employee workflows (time- off, swaps, reimbursements)	S	P	S	S
Notifications (shift reminders, approvals)	S	P	S	S
Testing & bug fixing	-	S	S	P
Documentation	P	S	P	S
Final demo & submission	P	S	S	S

P = Primary

S = Secondary

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Project Manager / Technical Lead	Charlie Langmuir	CL	2026-01-28
Software Developer	Joel Chandra Paul	JCP	2026-01-28
Business Analyst	Yueyang Peng	YP	2026-01-28
Quality Assurance / Testing Lead	Jingyu He	JH	2026-01-28
